

















































ID	Task Name	Duration	Start	Finish	Predecessors	19 Jun	Qtr 3, 2019 Jul Aug Sep	Qtr 4, 2019 Oct Nov Dec	Qtr 1, 2020 Jan Feb Mar	Qtr 2, 2020 Apr May Jun	Qtr 3, 2020 Jul Aug Sep	Qtr 4, 2020 Oct Nov
1	Quality Management Plan	350 days	Fri 19-07-19	Thu 19-11-20								
2	Preparation of Quality Management Plan	8 days	Fri 19-07-19	Tue 30-07-19								
3	Establish Test standard	4 days	Fri 19-07-19	Wed 24-07-19								
4	Establish Quality Assurance Plan	6 days	Fri 19-07-19	Fri 26-07-19	3SS							
5	Define Project Acceptance Criteria	5 days	Fri 19-07-19	Thu 25-07-19	4SS							
6	Construction of channel to divert the city drain	80 days	Tue 30-07-19	Mon 18-11-19	5,2							
7	Approval of Layout	11 days	Wed 31-07-19	Wed 14-08-19								
8	Construction Management Plan	21 days	Wed 31-07-19	Wed 28-08-19	7SS							
9	Construction methodology approval	10 days	Wed 31-07-19	Tue 13-08-19	8SS							
10	Approval of technical spec	12 days	Wed 31-07-19	Thu 15-08-19	9SS							
11	Procurement of Channel material	24 days	Fri 16-08-19	Wed 18-09-19	10							
12	Inspection of channel Material by Third party Inspection agency	46 days	Fri 16-08-19	Fri 18-10-19	11SS							
13	Construction of channel to divert the city drain	42 days	Fri 16-08-19	Mon 14-10-19	11SS							

Project: Project Date: Fri 01-05-20	Task	<div></div>	Inactive Summary	<div></div>	External Tasks	<div></div>
	Split	<div></div>	Manual Task	<div></div>	External Milestone	<div></div>
	Milestone	<div></div>	Duration-only	<div></div>	Deadline	<div></div>
	Summary	<div></div>	Manual Summary Rollup	<div></div>	Progress	<div></div>
	Project Summary	<div></div>	Manual Summary	<div></div>	Manual Progress	<div></div>
	Inactive Task	<div></div>	Start-only	<div></div>		
	Inactive Milestone	<div></div>	Finish-only	<div></div>		


ID	Task Name	Duration	Start	Finish	Predecessors	19 Jun	Qtr 3, 2019 Jul Aug Sep	Qtr 4, 2019 Oct Nov Dec	Qtr 1, 2020 Jan Feb Mar	Qtr 2, 2020 Apr May Jun	Qtr 3, 2020 Jul Aug Sep	Qtr 4, 2020 Oct Nov
14	Test on pressure piping used for creating drain channel	12 days	Tue 15-10-19	Wed 30-10-19	13							
15	Leakage test for pressure piping used for creating drain channel	3 days	Thu 31-10-19	Mon 04-11-19	14							
16	Manhole & catch Basin leakage testing which is an integral part of drain channel	3 days	Thu 31-10-19	Mon 04-11-19	15SS							
17	Inspection release note issued by Third Party Inspection agency	3 days	Tue 05-11-19	Thu 07-11-19	16							
18	Construction work inspection	3 days	Thu 31-10-19	Mon 04-11-19	15SS							
19	Testing of smooth drainage system	12 days	Thu 31-10-19	Fri 15-11-19	15SS							
20	Dredging (mud cleaning)	90 days	Mon 18-11-19	Fri 20-03-20	19,6							
21	Inspection of dredging equipment	6 days	Mon 25-11-19	Sat 30-11-19								
22	Physical inspection of mud cleaning process	72 days	Mon 02-12-19	Tue 10-03-20	21							
23	Lake Cleaning through biological treatment	132 days	Sun 01-12-19	Sun 31-05-20	21,20							

Project: Project Date: Fri 01-05-20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors	19 Jun	Qtr 3, 2019 Jul Aug Sep	Qtr 4, 2019 Oct Nov Dec	Qtr 1, 2020 Jan Feb Mar	Qtr 2, 2020 Apr May Jun	Qtr 3, 2020 Jul Aug Sep	Qtr 4, 2020 Oct Nov
24	Test on Dosing Chemicals used for lake cleaning	85 days	Mon 02-12-19	Fri 27-03-20	22SS							
25	Test of water quality	69 days	Mon 02-12-19	Thu 05-03-20	24SS							
26	Developing Nesting Islands	131 days	Thu 20-02-20	Thu 20-08-20	25SS,23							
27	Test on materials as well as construction for creating nesting islands	124 days	Mon 02-12-19	Thu 21-05-20	23SS							
28	Fountain installation in the lake	153 days	Thu 20-02-20	Sun 20-09-20	27SS,26SS							
29	Spec Creation for 4 Bubblers/fountain.	15 days	Sat 01-02-20	Thu 20-02-20								
30	Test of fountain Materials	52 days	Fri 21-02-20	Mon 04-05-20	29							
31	Test quality of lights and sound to be installed in the premise	73 days	Fri 21-02-20	Tue 02-06-20	30SS							
32	Performance test of fountains after installation	60 days	Wed 03-06-20	Tue 25-08-20	31							
33	Increasing Aquatic life to lake via scientific injection of new fish species	88 days	Mon 01-06-20	Wed 30-09-20	30,28SS							
34	Fish species Specification Approval	22 days	Mon 01-06-20	Tue 30-06-20								
35	Test on Biological oxygen of lake	44 days	Wed 01-07-20	Mon 31-08-20	34							

Project: Project Date: Fri 01-05-20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors	19 Jun	Qtr 3, 2019 Jul Aug Sep	Qtr 4, 2019 Oct Nov Dec	Qtr 1, 2020 Jan Feb Mar	Qtr 2, 2020 Apr May Jun	Qtr 3, 2020 Jul Aug Sep	Qtr 4, 2020 Oct Nov
36	Test on fish species before injection	44 days	Wed 01-07-20	Mon 31-08-20	35SS							
37	Testing of aquatic life after injection	22 days	Tue 01-09-20	Wed 30-09-20	36							
38	Plantation of Trees	250 days	Fri 01-11-19	Thu 15-10-20	19SS,33SS							
39	Testing of plant samples for creating wetland	108 days	Fri 01-11-19	Tue 31-03-20								
40	Test of soil for plantation of 500 trees around main lake area	125 days	Fri 01-11-19	Thu 23-04-20	39SS							
41	Plantation of Trees	109 days	Fri 24-04-20	Wed 23-09-20	40							
42	Final inspection by customer	9 days	Fri 01-11-19	Wed 13-11-19	38SS							
43	Handover and completion of project	0 days	Thu 14-11-19	Thu 14-11-19	42							

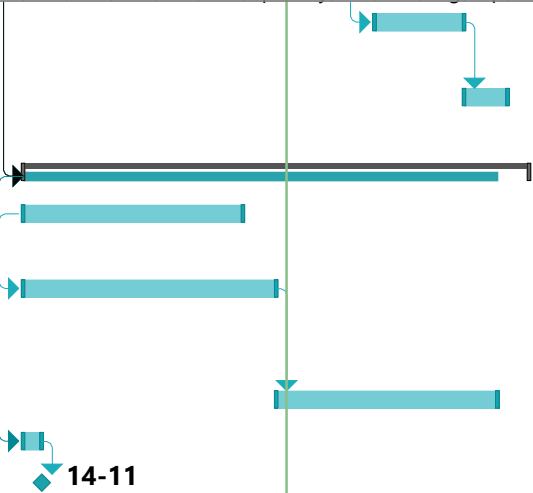

Project: Project
Date: Fri 01-05-20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
